

**HOFFMAN CONSTRUCTION COMPANY
OF OREGON**

**METRO HEADQUARTERS
Our Job No. 9214**

PROJECT MEETING MINUTES

Meeting No:	51	
Date:	December 8, 1992	
Location:	HCCO Field Office	
Attendees:	Glenn Taylor	Metro
	Maurice Neyma	Metro
	Bob Thompson	Thompson Vaivoda & Associates
	Paul Thimm	Thompson Vaivoda & Associates
	Darryl Droba	Glumac
	Cade Lawrence	Hoffman Construction Company
	Bill Stotts	Hoffman Construction Company
	Don Nail	Hoffman Construction Company

ACTION SUMMARY

HCCO
43-3-2 Get metal pricing to go with the Reception/Council desk low bid.
51-1-1 Check on standard fluorescent fixture delivery.

TVA
42-3-5 Get with city on final design approval of N. Plaza and approve deletion of glass.
47-3-4 Get with Desch and simplify Council fabric doors from 12/9/92, meeting.
48-3-2 Design a brochure rack into Reception desk from 12/9/92, meeting.
48-3-5 Issue an ASI to clarify electrical revisions for ADA.
48-3-6 Explain signage design to HCCO and Metro at 12/9/92 meeting.
49-3-2 Get the Parking Garage design in front of the city.
50-1-3 Review and select a final Daycare gym floor material.
50-1-4 Issue ASI to lower one (1) break room and Daycare sink casework.

METRO
✓ 48-3-4 Get with the city on Parking Garage backflow device.
48-3-6 Start on signage design.
✓ 50-3-1 Get with U.S. West on filling manhole.
50-3-7 Review Parking Garage elevator proposals.

51-1-0 ACTION ITEMS

✓ 51-1-1 FLUORESCENT FIXTURE BALLASTS: Glumac explained they had been contacted by the standard fluorescent fixture supplier requesting approval to revise the fixture ballast in order to meet the schedule. HCCO will check if there is a problem with the main 2 x 4 fixture delivery date.

Action: HCCO
Date: 12/11/92

SHIPPING THIS MONTH W/SPECIFIED BALLASTS.

✓ 51-1-2 ARTIST SCHEDULE: HCCO questioned the status of the artist schedule and contract. HCCO explained they are meeting with the artist on 12/9/92, to attempt finding a resolution to the cost and schedule issues.

Action: Metro
Date: 12/9/92

NEEDS ATTENTION

51-1-3 DAYCARE GYM FLOOR: Metro tabled samples of alternate Daycare gym floor materials which HCCO had submitted to them. TVA took the samples and will inform HCCO on 12/9/92, as to which material and color they select.

Action: TVA
Date: 12/9/92

51-2-0 RESOLVED ITEMS

47-2-6 TANK LIGHT FIXTURE: Metro questioned the status of TVA selecting a light fixture for the Tower tank. TVA will get started on selecting a fixture for the tank.

Action: TVA
Date: 11/17/92

As of November 24, 1992: Same as above.
As of December 1, 1992: Same as above.

VCT SPEC'D

R

As of December 8, 1992: TVA issued ASI #91 to clarify the type of light fixture at the Tower tank.

- 49-2-3 PARKING GARAGE FEEDER: HCCO explained they had received a VE request from Grasle to reuse the existing Parking Garage feeder. Metro explained it was acceptable to them if Glumac approved. HCCO will get the meggar tests over to Glumac so a decision can be made.

Action: HCCO/Glumac
Date: 12/1/92

As of December 1, 1992: Same as above.

As of December 8, 1992: Glumac confirmed there was no code reason for the Parking Garage main electrical feeder to be replaced if it meggar tested okay. Glumac did explain they recommended the feeder be replaced due to the fact that all other electrical feeding the garage was going to be new. HCCO acknowledged Glumac's concern but decided to proceed with reusing the existing feeder. Metro acknowledged HCCO action and just noted all warranty responsibilities would still need to be met.

- 50-2-2 LOW WALL RECEPTION CAP: Metro requested TVA revise the Reception area low wall cap to a greater width to allow paperwork to occur on top of wall cap. TVA will coordinate the cap width with Metro and issue an ASI.

Action: TVA/Metro
Date: 12/8/92

As of December 8, 1992: TVA issued ASI 85 to revise the low wall cap width as requested by Metro.

- 50-2-3 TRAFFIC DEMAND PLAN: HCCO questioned the status of city approval on the "Traffic Demand Plan" by Metro. Metro stated they believe the "Traffic Demand Plan" is approved and will send HCCO a copy.

Action: Metro
Date: 12/8/92

As of December 8, 1992: Metro issued HCCO a copy of the traffic demand plan for their use. HCCO will check with the city on approval and inform Metro if there is any problem.

- 50-2-5 U.S. WEST ROOM COST: Metro requested HCCO expedite the U.S. West room pricing. HCCO anticipated having a pricing proposal submitted by next week.

Action: HCCO
Date: 12/8/92

As of December 8, 1992: HCCO reported they submitted pricing to Metro on 12/7/92, for review and approval.

50-2-6 SLATE FLOOR EXTENSION: Metro requested the slate extension not proceed and that TVA revise the spine area to carpet with some special carpet designs. Metro will issue a RFP directing TVA to utilize carpet at the 2nd floor spine in lieu of slate.

Action: Metro/TVA
Date: 12/4/92

As of December 8, 1992: Metro issued RFP #20 requesting the second floor lobby slate extension not be exercised. HCCO informed TVA and the flooring subcontractors.

51-3-0 UNRESOLVED ITEMS

✓ 42-3-5 OVERALL SCHEDULE REVIEW: HCCO explained they are concerned about meeting the schedule deadline since the tenant square footage and dollar value had increased greatly without any schedule extension. All parties agreed the issue should be reviewed further, once the latest schedule is updated.

Action: HCCO/TVA
Date: 10/13/92

As of November 17, 1992: Metro approved awarding the Reception desk and Council Chambers' casework to John Earp. All parties discussed the N. Plaza design status and agreed to the following action items:

- a) TVA to issue an ASI simplifying the design and deleting the Plaza screen work.
- b) HCCO will obtain additional bids on the retail/trellis structural work.
- c) Metro approved the curtainwall design and HCCO will award to Harmon.
- d) TVA and HCCO will get with KPFF and try to reduce any special structural steel work.
- e) TVA will continue to pursue city (Edgar) approval.

As of November 24, 1992:

- a) Same as above.
- b) HCCO received bids over the Carr initial bid. HCCO awarded to Carr.
- c) HCCO awarded the work to Harmon.
- d) Same as above.
- e) Same as above.

As of December 1, 1992:

- a) TVA is to issue ASI on simplified trellis and Plaza screen.
- d) A meeting will be held at 9:30 today to finalize Plaza steel work.

- e) TVA will expedite city (Edgar) approval. Critical to small retail glass deletion.

As of December 8, 1992:

- a) TVA submitted for design review on 12/4/92. TVA issued ASI #86 to delete portions of the trellis tube steel.
- b) A meeting was held with the steel subcontractor, and Metro decided to leave all the steel in place.
- c) TVA will get with Edgar today and try to expedite a decision on deletion of the small retail space glass.

43-3-2

COUNCIL CHAMBERS DESK: TVA submitted the latest Council Chambers desk design to Metro for final approval. Metro will try to obtain approvals by 10/15/92, so TVA can issue "For Construction" drawings by 10/16/92. HCCO voiced concern this activity was going to be driving the schedule again if the work is not awarded by 10/16/92.

Action: Metro/TVA
Date: 10/16/92

As of November 24, 1992: HCCO explained John Earp could not get the casework completed as necessary to meet the schedule. HCCO obtained an updated bid from Desch, but their new bid was \$28,000 over the budget. All parties agreed HCCO would need to go out for more bids. HCCO will try to get more bids by 12/4/92. Metro to issued an RFP if they want Syndcrete.

As of December 1, 1992: HCCO explained they expect four (4) bids on 12/4/92, for the Reception desk and Council Chambers desk.

As of December 8, 1992: HCCO explained they received four (4) bids and have one (1) bidder (Alexander) which is below budget, but does not have the ironwork included. HCCO will get the bid updated with the ironwork. All parties agreed a meeting with Alexander should be held to review the quality of their work. HCCO set the meeting for 12/9/92 at 12:00 at TVA.

R
*AWARDED TO
ALEXANDER*

47-3-4 TACKABLE SURFACES: Metro reported that Homosote did not need to be used on the job. HCCO tabled pricing from Desch and Western Partitions in regards to the fabric panels and reviewed them with Metro. Metro will review the added work and decide if there are areas which can be cut.

Action: Metro
Date: 11/16/92

As of November 24, 1992: TVA issued ASI #77 to delete fabric panels at the conference rooms and No. Council Chambers' room. In regards to the original T.I. fabric, HCCO and Metro agreed to try for a less expensive fabric to reduce the dollar value of the claim by Western Partitions. HCCO will have new fabric samples sent over to TVA. TVA to work out sliding fabric door design with Desch.

As of December 1, 1992: HCCO had Maharam fabric submitted to TVA for review. TVA will review the fabric and settle with Desch on the sliding fabric door design.

As of December 8, 1992: HCCO explained Desch could get the sliding doors cost down to ±\$7,800 without the hardware and fabric included. TVA requested a meeting with Desch and HCCO set it up to occur on 12/9/92, at 11:00 at TVA. Metro will also attend. TVA will issue an ASI on the less expensive Knoll fabric selected by McCarter.

DOOR ASI ISSUED
\$9,500

48-3-2 BROCHURE RACK: Metro requested TVA add a small brochure rack to the Reception desk design so Metro pamphlets can be stored in that area. TVA will review the design and get a brochure rack added.

Action: TVA
Date: 11/24/92

As of November 24, 1992: Same as above.

As of December 1, 1992: Same as above.

As of December 8, 1992: TVA explained they are waiting for the reception desk to be awarded so they can work with the subcontractor on the brochure rack design. TVA will review this issue with the apparent low bidder on 12/9/92, at 12:00 at TVA.

TVA TO CHANGE SHOP DRAWINGS

✓ 48-3-4

GARAGE BACKFLOW: HCCO issued budget pricing to Metro on the new backflow device required by the city at the Parking Garage. Metro will review and call the city if they have any concerns about why it is being required.

Action: Metro
Date: 11/24/92

As of November 24, 1992: Same as above.
As of December 1, 1992: Same as above.
As of December 8, 1992: Same as above.

✓ 48-3-5

ADA REVIEW: HCCO issued the Professional Dynamics report concerning "ADA" to TVA for review and comment. TVA and Glumac will try to have a response ready by next week.

Action: TVA
Date: 11/24/92

As of November 24, 1992: TVA issued a response to the "ADA" review, and HCCO forwarded to Professional Dynamics for comment. TVA will expedite a response from Glumac.
As of December 1, 1992: Same as above. TVA will check on the Daycare drinking fountain meeting ADA requirements.
As of December 8, 1992: TVA reviewed the issue with Glumac and Glumac issued a memo dated 12/3/92, confirming the Daycare drinking fountain is accessible. Glumac did issue a response dated 12/1/92, concerning the overall "ADA" comments by Professional Dynamics. The electrical ADA issues were reviewed and TVA/Glumac will issue an ASI revising the strobes to 75 candella, adding an audio alarm at Council, adding an alarm at Fitness, etc.

Need ASI
GLUMAC!

48-3-6

SIGNAGE DESIGN: HCCO issued a fax requesting TVA and Metro start on the project signage design. Metro and TVA will get the process going.

Action: TVA/Metro
Date: 12/15/92

✓
As of November 24, 1992: TVA explained they will have a scheme for the main building sign by 12/1/92, with a preliminary scheme for the overall signage issued by 12/8/92.
As of December 1, 1992: Same as above with the exception of the main building sign to be issued to HCCO on 12/2/92.
As of December 8, 1992: TVA will review the signage design proposal with Metro and HCCO on 12/9/92, at 1:00 at TVA.

49-3-2 PARKING GARAGE DESIGN SUBMITTAL: TVA will meet with Edgar of the city on 11/25/92, and review the Parking Garage design so the overall design review can be completed. HCCO explained the electrical permit cannot be issued until design review is complete.

Action: TVA
Date: 11/25/92

As of December 1, 1992: Same as above. HCCO emphasized this issue is critical since the light fixtures were ordered and it would be prudent to confirm city approval.

As of December 8, 1992: TVA will inform Edgar (city) the Gardco fixture has been ordered, and he would need to inform Metro immediately if he still had any concerns. TVA will contact the city (Edgar) today, if possible.

SUBMISSION MADE 12/3/92

✓ 50-3-1 DAYCARE VAULT/MANHOLE: Metro will get with U.S. West regarding their schedule for filling the telephone vault with sand.

Action: Metro
Date: 12/8/92

As of December 8, 1992: Metro contacted U.S. West but has not received a response on when they can do the fill work.

50-3-4 ADA CASEWORK HEIGHT: Metro voiced concern regarding the Lounge and miscellaneous office coffee bars not being the proper "ADA" height. TVA explained they were in compliance with the basic intent of the ADA, but there were areas not totally accessible to handicap people. Metro requested all the basic coffee bars be totally accessible and will issue an RFP requesting such action.

Action: Metro
Date: 12/3/92

ISSUED
As of December 8, 1992: HCCO explained the second, third, and fourth floors casework are all fabricated at this time with the Daycare and Tower areas going into production this week. Metro requested TVA issue an ASI to lower the fourth floor break room and Daycare room casework which had sinks. TVA will expedite to prevent Desch from misfabricating.

ASI ISSUED.

✓ 50-3-7 PARKING GARAGE ELEVATOR: HCCO questioned the status of the Parking Garage elevator issue. Metro will review the old Parking Garage elevator proposals and get back with HCCO on how they want to proceed.

Action: Metro
Date: 12/8/92

As of 12/8/92: Same as above.

HCCO TO CHECK POWER TO ELEVATOR

51-4-0 QUALITY/SAFETY ITEMS

51-4-1 SAFETY MANHOURS: HCCO reported they had presently worked approximately 97,000 manhours without a lost time accident as of 12/1/92. 102,000 MHES

51-4-2 QUALITY ISSUES: No quality issues were brought up at the meeting.

51-5-0 INFORMATION ITEMS

51-5-1 NEXT MEETING: The next Project Review meeting is scheduled for 12/15/92, at 8:00 a.m. at the jobsite office.

51-5-2 SCHEDULE: See attachment, Figure #1 for a copy of the HCCO three-week schedule. See attachment, Figure #2 for a copy of the latest ASI log from TVA.

Submitted by:

Cade Lawrence


Cade Lawrence
Assistant Operations Manager

CL:gac

Attachments

cc: Attendees
Wayne Drinkward, HCCO
Berit Stevenson, Metro

COMPUTER ROOM

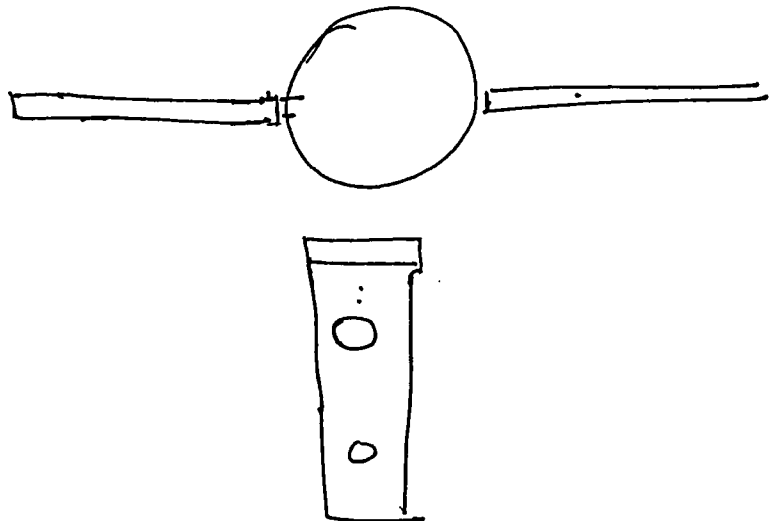

Attachment,
Fig. #1

Hoffman Construction Job # 9214
Short Interval Schedule
METRO HEADQUARTERS

ACTIVITY DESCRIPTION	Subcent.	DECEMBER																				
		7	8	9	10	11	12	13	14	15	16	17	18		19	20	21	22	23	24	25	
FRP SLAB ON DECK AT N.W. STAIR																	X	X	X	X	H	WAITING ON STRUCT STEEL
MISC. DEMOLITION	HSI		X	X	X	X	X															FOR NEW STEEL BEAMS
DEMO OLD FRP ELEV WALLS	HSI		X	X	X	X	X			X	X	X	X	X								AS NEW BEAMS ARE INSTALLED
FRP PEN NOR CONCRETE	HSI		X	X	X	X	X			X	X	X	X	X		X	X	X	X	X		AS AREAS ARE AVAILABLE
FRP FOUNDATION WALL AT N.W. CORNER	HSI		X	X	X	X	X															
POUR MISC INFILLS	HSI		X	X	X	X	X			X	X	X	X	X	X							
CERAMIC TILE AT TOILET ROOMS	PCI		X	X	X	X	X			X	X	X										
INSTALL ELEVATOR #3	SOUND		X	X	X	X	X			X	X	X	X	X		X	X	X	X	X		
INSTALL BRICK NEAR LOADING DOCK	DAVIDSON				X	X	X			X	X	X	X	X		X	X	X	X	X		
CMU AND BRICK AT PLANTERS	DAVIDSONS		X	X	X	X	X			X	X	X	X	X								NORTH AND SOUTH PLAZA
INSTALL WEST ELEVATION BRICK	DAVIDSON		X	X	X	X	X			X	X	X	X	X								WAITING ON STRUCT STEEL
INSTALL NORTH ELEVATION BRICK	DAVIDSON		X	X	X	X	X			X	X	X	X	X								WALL AT N.E STAIRWELL
COPE FLASHING AND STANDING SEAM METAL ROOF	MCBRIDE		X	X	X	X	X															CRITICAL
INSTALL CAULKING AT TOWER	HARMON		X	X	X																	
INSTALL NORTH ELEVATION CURTAINWALL	HARMON		X	X	X	X	X															AND PUNCHED OPENINGS
INSTALL ENTRYS	HARMON		X	X	X	X	X			X	X	X	X	X								AND ANNEX WINDOW
FIREPROOFING	PERFORMANCE		X	X	X	X	X			X	X	X	X	X								INTERMITTENT
INSULATION AND DRYWALL AND TAPE CORE AND SHELL	PERFORMANCE		X	X	X	X	X			X	X	X	X	X								START 3RD FLOOR 2ND FLOOR AND 1ST FLOOR

Hoffman Construction Job # 9214
 Short Interval Schedule
 METRO HEADQUARTERS

		DECEMBER																										
ACTIVITY DESCRIPTION	Subcont.	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25								
SCREENWALL AND DRYVIT	PERFORMANCE	X	X	X	X	X			X	X	X	X	X															WEATHER PERMITTING
STAIR #3 FRAME AND DRYVIT AND SHAFTWALL	PERFORMANCE	X	X	X	X	X			X	X	X	X	X															WEATHER PERMITTING
SITE ELECTRICAL	GRASLE	X	X	X	X	X																						LIGHT POLE BASES
ELECTRICAL ROUGHIN	JWP GRASLE	X	X	X	X	X			X	X	X	X	X				X	X	X	X	X							BRANCH CONDUIT AND WIRING
PLUMBING ROUGHIN AND TESTING	PEN NOR	X	X	X	X	X																						FIRST FLOOR
INSTALL AND INSULATE DUCT WORK	MCKINSTRY	X	X	X	X	X																						
STARTUP HVAC UNIT #1	MCKINSTRY																											AND DAYCARE UNIT
STAIR #6	CARR	X	X	X																								
LOADING DOCK FRAMES	CARR	X	X	X																								
CMU DEFLECTION HEADS	CARR																											FILL IN
STAIR SHAFT BEAMS	CARR	X	X																									
TRELLIS F TO C.5	CARR									X	X	X	X	X														
UPPER RETAIL	CARR									X	X	X	X	X														
ELEVATOR PIT LADDER	CARR					X	X																					
SITE CONCRETE GRADING AND PAVING	GOLDIE GENTLE	X	X	X	X	X			X	X																		WEATHER PERMITTING
GRADE AND POUR SIDEWALK AT PARKING GARAGE	VAN LOM	X	X	X	X	X			X																			NEED POWER POLES REMOVED
BRICK AND WINDOW FRAME CAULKING	HARMON PARDUE	X	X	X	X	X			X	X	X	X	X															AS WEATHER ALLOWS

Hoffman Construction Job # 9214
 Short Interval Schedule
 METRO HEADQUARTERS

		DECEMBER																																			
ACTIVITY DESCRIPTION	Subcont.	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25																	
	TI WORK	TI					TI					TI																									
FRAME, DRYWALL AND TAPE WALLS AND SOFFITS	WESTERN	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	START ON 3RD FLOOR THEN 2ND THEN 1ST AND ANNEX																
SET H.M. FRAMES	WESTERN	X	X	X	X	X																				2ND FLOOR AND SPINE											
COUNCIL CHAMBERS WALL FRAMING AND SOFFIT	WESTERN	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	AND GYP AND TAPING																
DAYCARE DRYWALL/TAPING	WESTERN	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	AND ANNEX																
COUNCIL CHAMBERS SPRINKLER RI	BASIC	X	X	X																																	
COUNCIL CHAMBERS CEILING ROUGHIN	GRASLE	X	X	X	X	X																															
ELECTRIC ROUGHIN CEILINGS/INSTALL LIGHT FIXTURES	GRASLE	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	3RD FLOOR, 1ST FLOOR																
ELECTRIC ROUGHIN WALLS AND CEILINGS	GRASLE	X	X	X	X	X			X	X	X	X	X																				2ND FLOOR AND FIRST FLOOR AND DAYCARE				
TI DUCT AND INSULATE	MCKINSTRY	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	2ND FLOOR, 1ST FLOOR AND DAYCARE																
PRIME COAT PAINT DRYWALL	REICHLE	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	3RD FLOOR THEN 2ND																
COMMUNICATION ROUGHIN	BROADWAY	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	2ND FLOOR, 1ST, DAYCARE																
DAYCARE PLUMBING AND TESTING	PEN NOR	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X																	
CEILING GRID	PCI	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	3RD FLOOR THEN 2ND FLOOR																
INSTALL SPINE GUARDRAILS	WELDCRAFT	X	X	X	X	X			X	X	X	X																									

ASI No.	DESCRIPTION	CONSULTANT RESPONSIBLE	DATE ISSUED	CROSS REFERENCE	STATUS
01	Revise brick dim. at tower entry	TVA	5-18-92		
02	East wall mod. for Penthouse	TVA	5-27-92	RFI-138	
03	Structural Items additional	KPFF	5-26-92		
04	M.S. backup at brick	TVA/KPFF	5-27-92		
05	Various Mech & Plumbing items	GLUMAC	5-27-92		
06	Clar.M.S. at stair tower	TVA	5-28-92		
07	Brick R.O. dim. change	TVA	5-29-92		
08	Brick Veneer East	TVA	6-2-92		
09	Misc. Arch. items	TVA	6-8-92		
10	Revise CMU, N. plaza demo, etc.	TVA	6-18-92		
11	Plancheck Architectural comments	TVA	6-12-92		
12	Brick veneer mod. for (e) cond.	TVA	6-16-92		
13	Alum. closure mod. / insul. change	TVA	7-13-92		
14R	Core & Shell revision due to T.I.	TVA	7-16-92		REV. 7-24-92
15	New plate at window head	TVA	7-22-92		
16	Channel at offset loc.	TVA	7-24-92		
17	Elec. main service conduit changes	GLUMAC	7-27-92		
18	Curtainwall metal panels / tie rods	TVA	7-28-92		
19	Move 2' x 2' wdw. on west elev.	TVA	7-28-92		
20	Tower structure cladding anchors	KPFF	7-29-92		
21	36 x 72 hole for penthouse mech.	KPFF	7-30-92		
22	Various M. & E. per Glumac mtg.	GLUMAC	8-3-92		
23	Cast Stone Ornament	TVA	8-4-92		
24	Partition Clarifications	TVA	8-7-92		
25R	T.I. Revisions per METRO	TVA/GLUMAC	9-30-92		REV. 9-30-92
26	Roof screen changes	TVA	8-12-92		
27	T.I. Elec. & Phone changes	GLUMAC/ACSi	8-13-92		
28	Door and louver relocation at tower	TVA	8-14-92		
29	Stair #3 tower parapets	TVA	8-17-92		
30	Delete cable tray at north plaza	GLUMAC	8-19-92		
31	Paver joint and aggregate conc. clarify	TVA	8-26-92		
32	Elevator Pit Lights	GLUMAC	8-31-92		
33	T.I. Plancheck items	TVA	9-9-92		
34	T.I. Wd to H.M. frame substitution	TVA	9-9-92		T.I. V.E.
35	Add 2 roof drains at plaza retail	GLUMAC	9-14-92		
36	Decorative stone medallions locations	TVA	9-15-92		
37	Openings in Park. Stru. shearwalls	TVA/KPFF	9-16-92	RFI-192	
38	Flagpole layout & support clarification	TVA/KPFF	9-18-92		
39	Plumbing changes in bsmt.	GLUMAC	9-18-92		
40	Landscape VE & METRO changes	MAYER-REED	9-22-92		T.I. V.E.
41R	New brick at auto entry wall	TVA	9-24-92		REV. 11-5-92
42	Plaza plancheck, etc.	TVA	11-16-92		
43	T.I. 2nd & 3rd fl. ceiling revisions	TVA	9-28-92	ASI-48	SUPERSEDED
44	T.I. Fitness shower layout revision	TVA	9-28-92		
45	T.I. HVAC rev. at Council Ch.+ misc.	GLUMAC	10-2-92		
46	T.I. Light rev. + clarifications (Memo)	GLUMAC	10-5-92		
47	Stair 5 rail support modification	TVA/KPFF	10-8-92		
48	Coordinated Ceiling Plans 2nd + 3rd	TVA	10-9-92		REPLACES ASI.
49R	Media box & F.A. pnl locations	TVA	10-12-92		REV. 10-26-92
50	Sidewalk scoreline clarifications	TVA	10-8-92		

ASI No.	DESCRIPTION	CONSULTANT	DATE	CROSS	STATUS
		RESPONSIBLE	ISSUED	REFERENCE	
51	Landscape + irrig. for parking structure	MAYER/REED	10-12-92		
52	N. Plaza planter drains rev.	TVA/GLUMAC	10-13-92		
53	Daycare "dock" stair + rail clarification	TVA	10-15-92		
54	Plumbing rev. Sheet TP2.1 (field coord.)	GLUMAC	10-15-92		
55	Daycare kitchen revision	TVA/GLUMAC	10-16-92		(appeal hoo
56	Various T.I. V.E. items (combined)	TVA	10-19-92		T.I. V.E.
57	Lighting rev. + occ. sens. 2nd+3rd	GLUMAC	10-20-92		T.I. V.E.
58	Revise H.M. relites at rm. 201A	TVA	10-20-92	ASI-34	T.I. item
59	T.I. finish schedule	TVA	10-21-92	See ASI-74	T.I. item
60	Police T.I. docs. + Fitness revision	TVA/GLUMAC	10-21-92		T.I. item
61	Add Fiber optic phone equip. rm.	TVA	11-16-92		For US WE
62	Roof Appeal - add phone, ch. hardware	TVA	10-26-92		METRO req
63	Change to dimmable lights council chamber	GLUMAC	10-27-92	PR-4	ASI-66
64	Misc. mechanical rev. 2nd + 3rd	GLUMAC	11-2-92		
65	Park structure railings + paint	TVA	11-5-92		
66	AV room 362 revisions	TVA/GLUMAC	11-3-92	PR-4	ASI-63
67R	Recycled paint scheme clarification	TVA	REV. 11/12/9	PR-5+6	Void per ASI-75
68	Council desk, kitchen + add toilet	TVA	11-9-92	PR-7	T.I. item
69	VE wood wall caps to MDF	TVA	11-6-92		T.I. V.E.
70	Misc. elec. and mech. items	TVA/GLUMAC	11-6-92		
71	Extend slate flooring in lobby	TVA	11-16-92	PR-8	T.I. item
72	Rev. low wall at rm. 385, etc.	TVA	11-16-92	PR-2	T.I. item
73	Add access at roof screen at RAC-1	TVA	11-17-92	Glumac field report	
74R	P.lam changes/VCT pattern/carpet spec	TVA	11-17-92	PR-12	REV. 11/24/92
75	Clarify sawcut & alum. at daycare south	TVA	11-18-92		T.I. item
76	Delete finish in stairs 3 + 4	TVA	11-23-92		T.I. V.E.
77	Delete tack bd. at 3 rooms	TVA	11-23-92	PR-15	T.I. V.E.
78	Delete refer. at room 382 (O.F.O.I.)	TVA	11-23-92	PR-16	T.I. V.E.
79	Revise again recycle paint scheme	TVA	11-23-92	PR-14	replace ASI
80	Add power to main phone room	TVA	11-24-92	PR-11	
81	Mod cab. + wall see-thru room 297	TVA	11-25-92	PR-9	
82R	W.H. + casewk changes, rm. 359, 401	TVA/GLUMAC	11-25-92		REV. 11/30/92
83	Delete curtainwall X-brace rods	TVA	11-25-92		
84	Modify duct size at council chamber	GLUMAC	11-30-92		field problem
85	Add wide cap at 42" part. + clar. det.	TVA	12-2-92	PR-___	
86	Delete some steel at N. Plaza trellis	TVA	12-2-92		T.I. V.E.
87	Clarify wood base loc.	TVA	12-2-92		T.I. V.E.
88	Change M.P. to spandrel at Plaza retail	TVA	12-4-92		T.I. V.E.
89	V.E. fire alarm cable system	HCCO	12-4-92	PR-17	T.I. V.E.
90	Filter fabric + Grimms soil mix change	MAYER/REED	12-4-92	PR-18	
91	Spec. light fixture at 601 - tank room	TVA	12-4-92		
92					
93					
94					
95					
96					
97					
98					
99					
